
MANAGER USER GUIDE

OMRAN ERP

A premium, practical guide for managing construction projects from AI intake to execution, monitoring, and invoicing.

AI-assisted construction management


Manager workflow



System at a glance


What OMRAN helps the manager control

OMRAN is a mini ERP for construction and renovation projects. It connects project intake, proposal generation, workshop assignment, execution tracking, AI monitoring, and invoices into one controlled workflow.



End-to-end manager workflow

The complete path from conversation to official project data

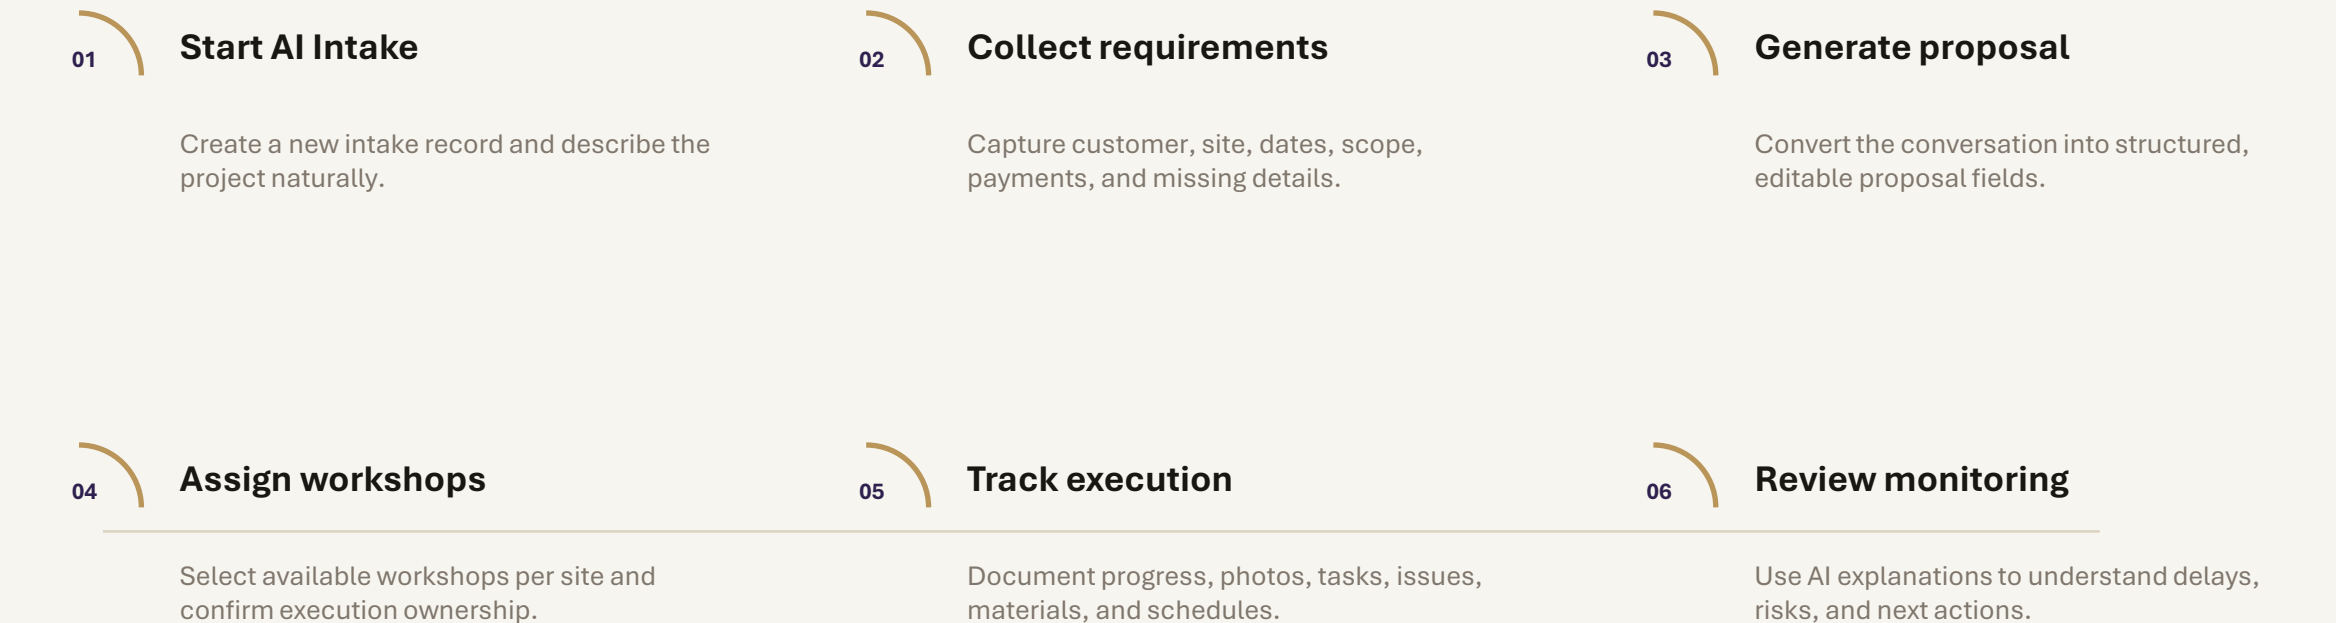

AI Intake

A natural conversation instead of a rigid form

Start a new intake

Open AI Intake and select New. Describe the project using normal language — customer, location, responsible person, dates, and required work areas.

Use voice when available

Voice-to-text can capture spoken notes from the office or site, then send the content into the same AI intake workflow.

Example project input

“We have a renovation project for Al-Sham Development in Damascus. The main contact is Ahmad Mansour. The kitchen needs tile replacement and plumbing fixes. The main bathroom needs waterproofing and sanitary work.”

- The assistant asks only for missing practical details.
- Sessions stay isolated and editable.
- Manager remains in control before confirmation.

Define the scope of work

Turn site details into structured execution requirements

After basic project information is captured, enter work details by location or area. OMRAN extracts the operational structure needed for proposal and execution.

Work location	Kitchen, bathroom, living room, facade, roof
Work type	Tiles, waterproofing, painting, electrical, sanitary
Required skills	Workshop expertise and execution capabilities
Materials	Paint, ceramic, insulation, fixtures, supplies
Missing data	Questions that need manager confirmation


Manager rule

Write scope in normal language. The system organizes it, but the manager reviews what becomes official.

Good input → better proposal → stronger tracking.

Proposal generation

AI organizes information; the manager approves the official version

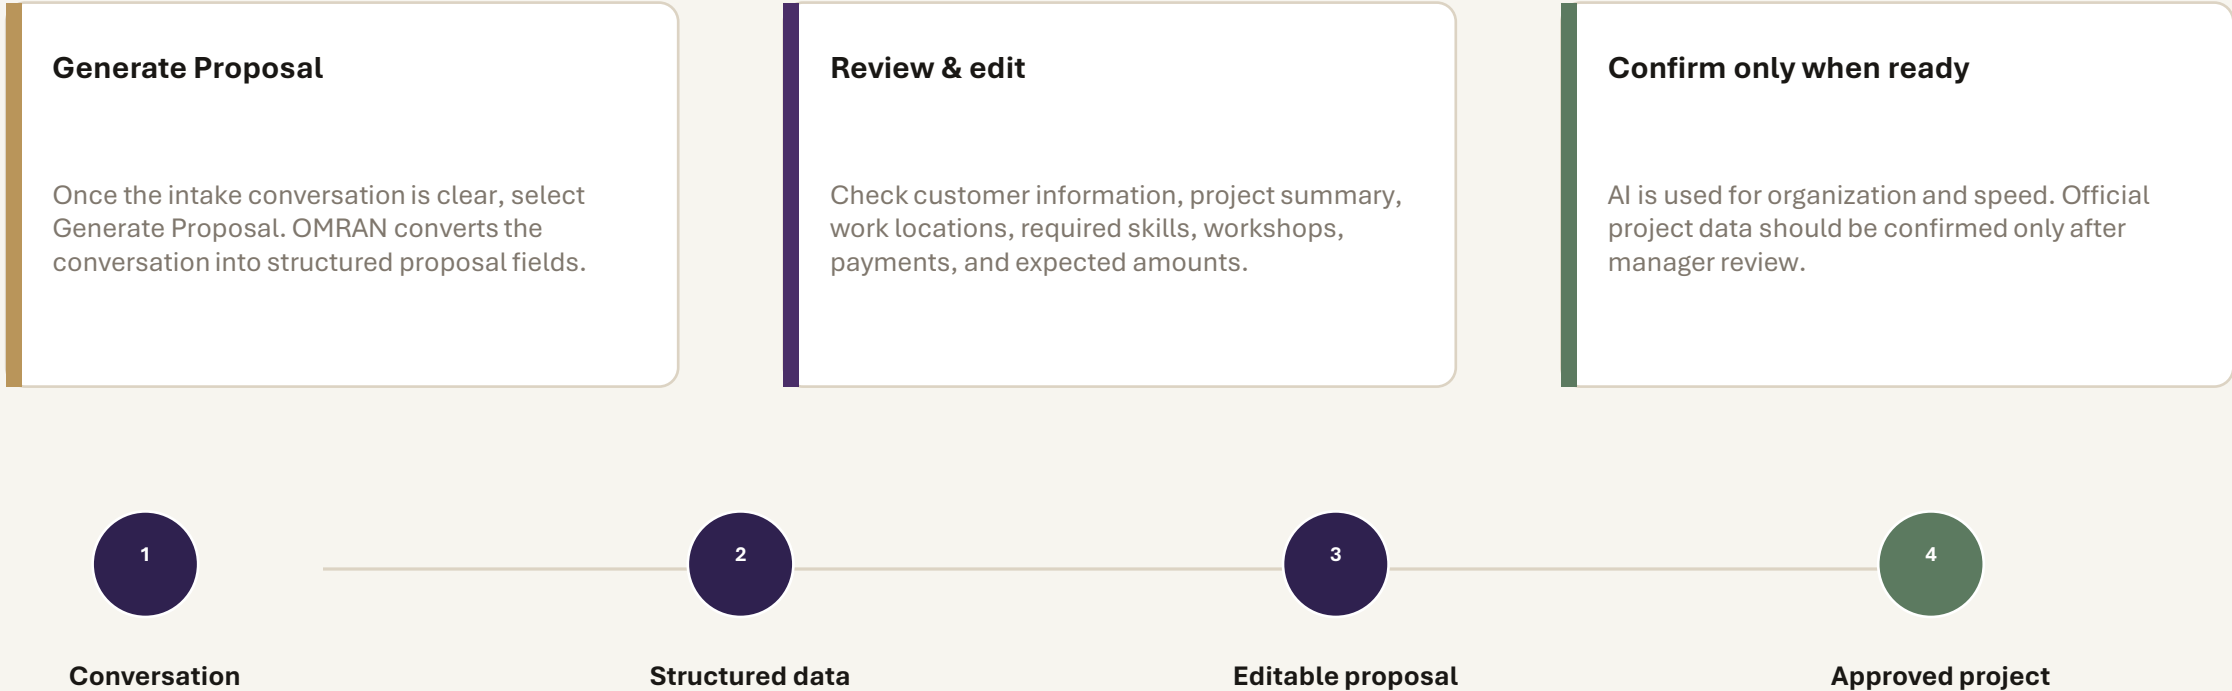

Workshops

External workshops are the core execution model

Workshop selection

- Review each work location.
- Assign the responsible workshop.
- Check whether the workshop covers the required skills.
- If none is suitable, mark the location as Workshop needed.

Workshop management

- Add or edit workshop profile.
- Define specialties such as tiles, waterproofing, painting, electrical, or sanitary work.
- Set availability as Available or Not Available.
- Unavailable workshops are not suggested for execution.

Convert proposal to order

This is where a draft becomes an official project

After the manager reviews the proposal and workshop assignments, the system can convert the proposal into an official order. From that point, the project becomes trackable.

Confirm

Manager accepts the reviewed proposal.

Create Order

System creates the official project record.

Open Control Pages

Order Detail, Project Tracking, AI Monitoring, and Invoices become available.

Control principle: drafts are flexible; orders are operational records.

Project Tracking

The daily execution control center

Open an order, then select Open Tracking. This page documents execution manually and provides the data AI Monitoring needs to give reliable explanations.

Progress overview

Current completion and status

Baseline schedule

Official plan for each site

Timeline updates

Execution notes over time

Photos

Visual evidence from site

Tasks

Weighted work items

Issues

Blockers and resolution status

Materials

Needed, ordered, delivered, used

Workshop schedule

Execution coordination

Daily execution data

Tasks, issues, materials, and updates make the project measurable

Tasks

Create tasks per location. Set status, owner, due date, weight, and progress percentage. Weight reflects the importance of the task inside location progress.

Issues

Record blockers with severity, owner, location, status, and resolution notes. Open issues appear in warnings and affect monitoring.

Materials

Track ceramic, paint, waterproofing, fixtures, electrical or sanitary supplies by quantity, location, status, and notes.


Example update

“The old bathroom tiles have been removed and the floor is ready for the first waterproofing layer.”

Baseline schedule

The official reference for delay analysis

Baseline is the confirmed plan for work locations inside a project. AI Monitoring relies on confirmed baseline dates, not just drafts.

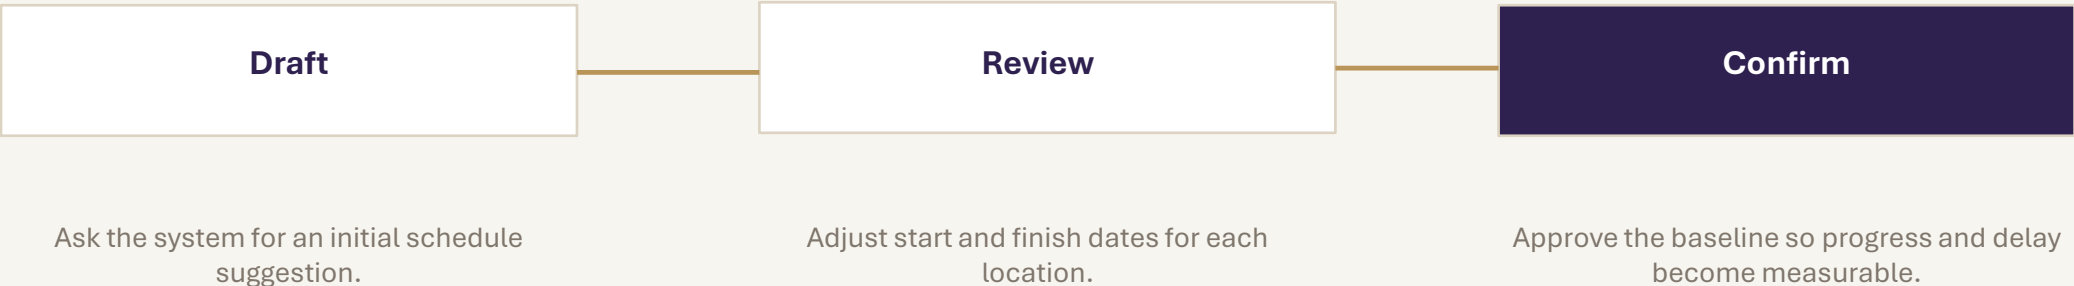

No confirmed baseline → weaker delay analysis.

AI Monitoring

Explanations based on structured tracking data

AI Monitoring explains the project health using backend-calculated values and tracking data. It does not invent official numbers.

- Planned vs actual progress
- Progress gap and delay status
- Expected finish date
- Open issues and blockers
- Missing information
- Recommended next actions

Monitoring logic

Tracking data + confirmed baseline + open issues + material status → clear project-health explanation for the manager.

Better input data creates stronger AI analysis.

Invoices and payments

Financial follow-up remains reviewable and controlled

The Invoices page lets the manager create, review, edit, export, and follow payment status. Invoices are connected to project, locations, and invoice items rather than internal employee hours.

Create invoice

Build invoice items from the project scope and locations.

Review status

Edit invoice status, payment progress, and details before export.

Export

Generate PDF or Word outputs for operational documentation.

Invoices are business records. Review amounts, dates, and items before sending.

Recommended daily routine

A simple operating rhythm for the manager

- Review Dashboard for the global situation.
- Open active Orders.
- Open Tracking for the project that needs attention.
- Add updates, photos, tasks, issues, and material status.
- Review AI Monitoring for risks and next actions.
- Update workshops, baseline, invoices, or payments as needed.

Golden rule

The system helps the manager organize and decide. It does not replace the manager's review.

Before approving any proposal, invoice, or execution plan, review prices, dates, scope, workshops, payments, and warnings.
